

## WATERS (GROUND WATER BASINS)

ID	Task Name	Duration	Start	Finish	% Complete	2003				2004				2005				2006				2007				2008				2009
						Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1
1	<b>Fort Sumner GWB</b>	<b>73 days</b>	<b>Wed 1/15/03</b>	<b>Mon 4/28/03</b>	<b>100%</b>																									
2	Organizational Meetings	5 days	Wed 1/15/03	Wed 1/22/03	100%																									
3	Preparation of Project Plan	20 days	Thu 1/23/03	Wed 2/19/03	100%																									
4	Sort and Compare	104 hrs	Thu 2/20/03	Mon 3/10/03	100%																									
5	Abstract File	215 hrs	Tue 3/11/03	Wed 4/16/03	100%																									
6	QA and Archive	65 hrs	Wed 4/16/03	Mon 4/28/03	100%																									
7	<b>Hot Springs GWB</b>	<b>33 days</b>	<b>Wed 1/15/03</b>	<b>Mon 3/3/03</b>	<b>100%</b>																									
8	Organizational Meetings	5 days	Wed 1/15/03	Wed 1/22/03	100%																									
9	Preparation of Project Plan	20 days	Thu 1/23/03	Wed 2/19/03	100%																									
10	Sort and Compare	16 hrs	Thu 2/20/03	Fri 2/21/03	100%																									
11	Abstract File	32 hrs	Mon 2/24/03	Thu 2/27/03	100%																									
12	QA and Archive	8 hrs	Mon 3/3/03	Mon 3/3/03	100%																									
13	<b>Hueco GWB</b>	<b>53.38 days</b>	<b>Wed 1/15/03</b>	<b>Tue 4/1/03</b>	<b>100%</b>																									
14	Organizational Meetings	5 days	Wed 1/15/03	Wed 1/22/03	100%																									
15	Preparation of Project Plan	20 days	Thu 1/23/03	Wed 2/19/03	100%																									
16	Sort and Compare	5 hrs	Thu 2/20/03	Thu 2/20/03	100%																									
17	Abstract File	10 hrs	Thu 3/20/03	Fri 3/21/03	100%																									
18	QA and Archive	3 hrs	Tue 4/1/03	Tue 4/1/03	100%																									
19	<b>Las Animas Creek GWB</b>	<b>26.88 days</b>	<b>Wed 1/15/03</b>	<b>Fri 2/21/03</b>	<b>100%</b>																									
20	Organizational Meetings	5 days	Wed 1/15/03	Wed 1/22/03	100%																									
21	Preparation of Project Plan	20 days	Thu 1/23/03	Wed 2/19/03	100%																									
22	Sort and Compare	3 hrs	Thu 2/20/03	Thu 2/20/03	100%																									
23	Abstract File	7 hrs	Fri 2/21/03	Fri 2/21/03	100%																									
24	QA and Archive	2 hrs	Fri 2/21/03	Fri 2/21/03	100%																									
25	<b>Salt Basin GWB</b>	<b>26.75 days</b>	<b>Wed 1/15/03</b>	<b>Fri 2/21/03</b>	<b>100%</b>																									
26	Organizational Meetings	5 days	Wed 1/15/03	Wed 1/22/03	100%																									
27	Preparation of Project Plan	20 days	Thu 1/23/03	Wed 2/19/03	100%																									
28	Sort and Compare	3 hrs	Thu 2/20/03	Thu 2/20/03	100%																									
29	Abstract File	6 hrs	Fri 2/21/03	Fri 2/21/03	100%																									
30	QA and Archive	2 hrs	Fri 2/21/03	Fri 2/21/03	100%																									
31	<b>Tularosa GWB</b>	<b>239.38 days</b>	<b>Wed 1/15/03</b>	<b>Mon 12/29/03</b>	<b>100%</b>																									
32	Organizational Meetings	5 days	Wed 1/15/03	Wed 1/22/03	100%																									
33	Preparation of Project Plan	20 days	Thu 1/23/03	Wed 2/19/03	100%																									
34	Sort and Compare	68 hrs	Thu 2/20/03	Tue 3/4/03	100%																									
35	Abstract File	141 hrs	Wed 5/28/03	Fri 6/20/03	100%																									
36	QA and Archive	43 hrs	Fri 12/19/03	Mon 12/29/03	100%																									
37	<b>Sandia GWB</b>	<b>105.63 days</b>	<b>Mon 6/23/03</b>	<b>Fri 11/21/03</b>	<b>100%</b>																									
38	Organizational Meetings	5 days	Mon 6/23/03	Fri 6/27/03	100%																									
39	Preparation of Project Plan	20 days	Mon 6/30/03	Mon 7/28/03	100%																									
40	Sort and Compare	174 hrs	Tue 7/29/03	Wed 8/27/03	100%																									
41	Abstract File	361 hrs	Wed 8/27/03	Fri 10/31/03	100%																									
42	QA and Archive	110 hrs	Fri 10/31/03	Fri 11/21/03	100%																									
43	<b>San Juan GWB</b>	<b>108.25 days</b>	<b>Mon 8/25/03</b>	<b>Fri 1/30/04</b>	<b>25%</b>																									
44	Organizational Meetings	5 days	Mon 8/25/03	Fri 8/29/03	100%																									
45	Preparation of Project Plan	20 days	Tue 9/2/03	Mon 9/29/03	100%																									
46	Sort and Compare	180 hrs	Tue 9/30/03	Fri 10/31/03	9%																									
47	Abstract File	373 hrs	Fri 10/31/03	Mon 1/12/04	0%																									
48	QA and Archive	113 hrs	Mon 1/12/04	Fri 1/30/04	0%																									

Project: WATERS  
Date: Thu 11/13/03

Task		Milestone		Rolled Up Task		Rolled Up Progress		External Tasks		Group By Summary	
Progress		Summary		Rolled Up Milestone		Split		Project Summary			

### WATERS (GROUND WATER BASINS)

ID	Task Name	Duration	Start	Finish	% Complete	2003				2004				2005				2006				2007				2008				2009			
						Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1			
49	<b>Virden Valley GWB</b>	<b>36.5 days</b>	<b>Tue 9/2/03</b>	<b>Thu 10/23/03</b>	<b>50%</b>	Virden Valley GWB 10/23/2003																											
50	Organizational Meetings	5 days	Tue 9/2/03	Mon 9/8/03	100%	Organizational Meetings																											
51	Preparation of Project Plan	20 days	Tue 9/9/03	Mon 10/6/03	66%	Preparation of Project Plan																											
52	Sort and Compare	25 hrs	Tue 10/7/03	Fri 10/10/03	0%	Sort and Compare																											
53	Abstract File	51 hrs	Fri 10/10/03	Tue 10/21/03	0%	Abstract File																											
54	QA and Archive	16 hrs	Tue 10/21/03	Thu 10/23/03	0%	QA and Archive																											
55	<b>Gallup GWB</b>	<b>55.63 days</b>	<b>Mon 9/15/03</b>	<b>Fri 12/5/03</b>	<b>0%</b>	Gallup GWB 12/5/2003																											
56	Organizational Meetings	5 days	Mon 9/15/03	Fri 9/19/03	0%	Organizational Meetings																											
57	Preparation of Project Plan	20 days	Mon 9/22/03	Mon 10/20/03	0%	Preparation of Project Plan																											
58	Sort and Compare	66 hrs	Tue 10/21/03	Fri 10/31/03	0%	Sort and Compare																											
59	Abstract File	137 hrs	Fri 10/31/03	Wed 11/26/03	0%	Abstract File																											
60	QA and Archive	42 hrs	Wed 11/26/03	Fri 12/5/03	0%	QA and Archive																											
61	<b>Upper Pecos GWB</b>	<b>82.13 days</b>	<b>Mon 9/29/03</b>	<b>Wed 1/28/04</b>	<b>0%</b>	Upper Pecos GWB 1/28/2004																											
62	Organizational Meetings	5 days	Mon 9/29/03	Fri 10/3/03	0%	Organizational Meetings																											
63	Preparation of Project Plan	20 days	Mon 10/6/03	Mon 11/3/03	0%	Preparation of Project Plan																											
64	Sort and Compare	123 hrs	Tue 11/4/03	Wed 11/26/03	0%	Sort and Compare																											
65	Abstract File	256 hrs	Wed 11/26/03	Wed 1/14/04	0%	Abstract File																											
66	QA and Archive	78 hrs	Wed 1/14/04	Wed 1/28/04	0%	QA and Archive																											
67	<b>Carlsbad GWB</b>	<b>196.25 days</b>	<b>Mon 10/27/03</b>	<b>Mon 8/2/04</b>	<b>84%</b>	Carlsbad GWB 8/2/2004																											
68	Organizational Meetings	5 days	Mon 10/27/03	Fri 10/31/03	100%	Organizational Meetings																											
69	Preparation of Project Plan	20 days	Mon 11/3/03	Wed 12/3/03	100%	Preparation of Project Plan																											
70	Sort and Compare	370 hrs	Thu 12/4/03	Mon 2/9/04	100%	Sort and Compare																											
71	Abstract File	767 hrs	Mon 2/9/04	Tue 6/22/04	98%	Abstract File																											
72	QA and Archive	233 hrs	Tue 6/22/04	Mon 8/2/04	0%	QA and Archive																											
73	<b>Lower Rio Grande GWB</b>	<b>111.63 days</b>	<b>Mon 11/10/03</b>	<b>Tue 4/20/04</b>	<b>80%</b>	Lower Rio Grande GWB 4/20/2004																											
74	Organizational Meetings	5 days	Mon 11/10/03	Tue 11/18/03	100%	Organizational Meetings																											
75	Preparation of Project Plan	20 days	Tue 11/18/03	Thu 12/18/03	100%	Preparation of Project Plan																											
76	Sort and Compare	187 hrs	Thu 12/18/03	Wed 1/21/04	100%	Sort and Compare																											
77	Abstract File	388 hrs	Thu 1/22/04	Tue 3/30/04	84%	Abstract File																											
78	QA and Archive	118 hrs	Tue 3/30/04	Tue 4/20/04	0%	QA and Archive																											
79	<b>Blue Water GWB</b>	<b>94.63 days</b>	<b>Fri 11/21/03</b>	<b>Wed 4/7/04</b>	<b>21%</b>	Blue Water GWB 4/7/2004																											
80	Organizational Meetings	5 days	Fri 11/21/03	Tue 12/2/03	100%	Organizational Meetings																											
81	Preparation of Project Plan	20 days	Tue 12/2/03	Wed 12/31/03	74%	Preparation of Project Plan																											
82	Sort and Compare	150 hrs	Wed 12/31/03	Tue 1/27/04	0%	Sort and Compare																											
83	Abstract File	312 hrs	Tue 1/27/04	Mon 3/22/04	0%	Abstract File																											
84	QA and Archive	95 hrs	Mon 3/22/04	Wed 4/7/04	0%	QA and Archive																											
85	<b>Estancia GWB</b>	<b>63 days</b>	<b>Wed 4/7/04</b>	<b>Mon 7/5/04</b>	<b>0%</b>	Estancia GWB 7/5/2004																											
86	Organizational Meetings	5 days	Wed 4/7/04	Wed 4/14/04	0%	Organizational Meetings																											
87	Preparation of Project Plan	20 days	Wed 4/14/04	Wed 5/12/04	0%	Preparation of Project Plan																											
88	Sort and Compare	82 hrs	Wed 5/12/04	Wed 5/26/04	0%	Sort and Compare																											
89	Abstract File	170 hrs	Wed 5/26/04	Thu 6/24/04	0%	Abstract File																											
90	QA and Archive	52 hrs	Thu 6/24/04	Mon 7/5/04	0%	QA and Archive																											
91	<b>Hondo GWB</b>	<b>200.63 days</b>	<b>Mon 8/2/04</b>	<b>Mon 5/9/05</b>	<b>0%</b>	Hondo GWB 5/9/2005																											
92	Organizational Meetings	5 days	Mon 8/2/04	Mon 8/9/04	0%	Organizational Meetings																											
93	Preparation of Project Plan	20 days	Mon 8/9/04	Mon 9/6/04	0%	Preparation of Project Plan																											
94	Sort and Compare	379 hrs	Mon 9/6/04	Wed 11/10/04	0%	Sort and Compare																											
95	Abstract File	787 hrs	Wed 11/10/04	Mon 3/28/05	0%	Abstract File																											
96	QA and Archive	239 hrs	Tue 3/29/05	Mon 5/9/05	0%	QA and Archive																											

Project: WATERS  
Date: Thu 11/13/03

Task		Milestone		Rolled Up Task		Rolled Up Progress		External Tasks		Group By Summary	
Progress		Summary		Rolled Up Milestone		Split		Project Summary			






### WATERS (GROUND WATER BASINS)

ID	Task Name	Duration	Start	Finish	% Complete	2003				2004				2005				2006				2007				2008				2009
						Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1
193	<b>Roswell Artesian GWB</b>	<b>461.75 days</b>	<b>Mon 1/9/23</b>	<b>Wed 10/16/24</b>	<b>19%</b>																									
194	Organizational Meetings	5 days	Mon 1/9/23	Mon 1/16/23	100%																									
195	Preparation of Project Plan	20 days	Mon 1/16/23	Mon 2/13/23	100%																									
196	Sort and Compare	943 hrs	Mon 2/13/23	Thu 7/27/23	53%																									
197	Abstract File	1957 hrs	Thu 7/27/23	Wed 7/3/24	0%																									
198	QA and Archive	594 hrs	Thu 7/4/24	Wed 10/16/24	0%																									
199	<b>San Simon GWB</b>	<b>31.5 days</b>	<b>Wed 10/16/24</b>	<b>Thu 11/28/24</b>	<b>0%</b>																									
200	Organizational Meetings	5 days	Wed 10/16/24	Wed 10/23/24	0%																									
201	Preparation of Project Plan	20 days	Wed 10/23/24	Wed 11/20/24	0%																									
202	Sort and Compare	14 hrs	Wed 11/20/24	Thu 11/21/24	0%																									
203	Abstract File	29 hrs	Fri 11/22/24	Wed 11/27/24	0%																									
204	QA and Archive	9 hrs	Wed 11/27/24	Thu 11/28/24	0%																									
205	<b>Tucumcari GWB</b>	<b>40.25 days</b>	<b>Thu 11/28/24</b>	<b>Thu 1/23/25</b>	<b>0%</b>																									
206	Organizational Meetings	5 days	Thu 11/28/24	Thu 12/5/24	0%																									
207	Preparation of Project Plan	20 days	Thu 12/5/24	Thu 1/2/25	0%																									
208	Sort and Compare	33 hrs	Thu 1/2/25	Wed 1/8/25	0%																									
209	Abstract File	68 hrs	Wed 1/8/25	Tue 1/21/25	0%																									
210	QA and Archive	21 hrs	Tue 1/21/25	Thu 1/23/25	0%																									

Project: WATERS Date: Thu 11/13/03	Task  Milestone Progress  Summary	Rolled Up Task Rolled Up Milestone	Rolled Up Progress Split	External Tasks Project Summary	Group By Summary
---------------------------------------	--------------------------------------	---------------------------------------	-----------------------------	-----------------------------------	------------------

### WATERS (GROUND WATER BASINS)

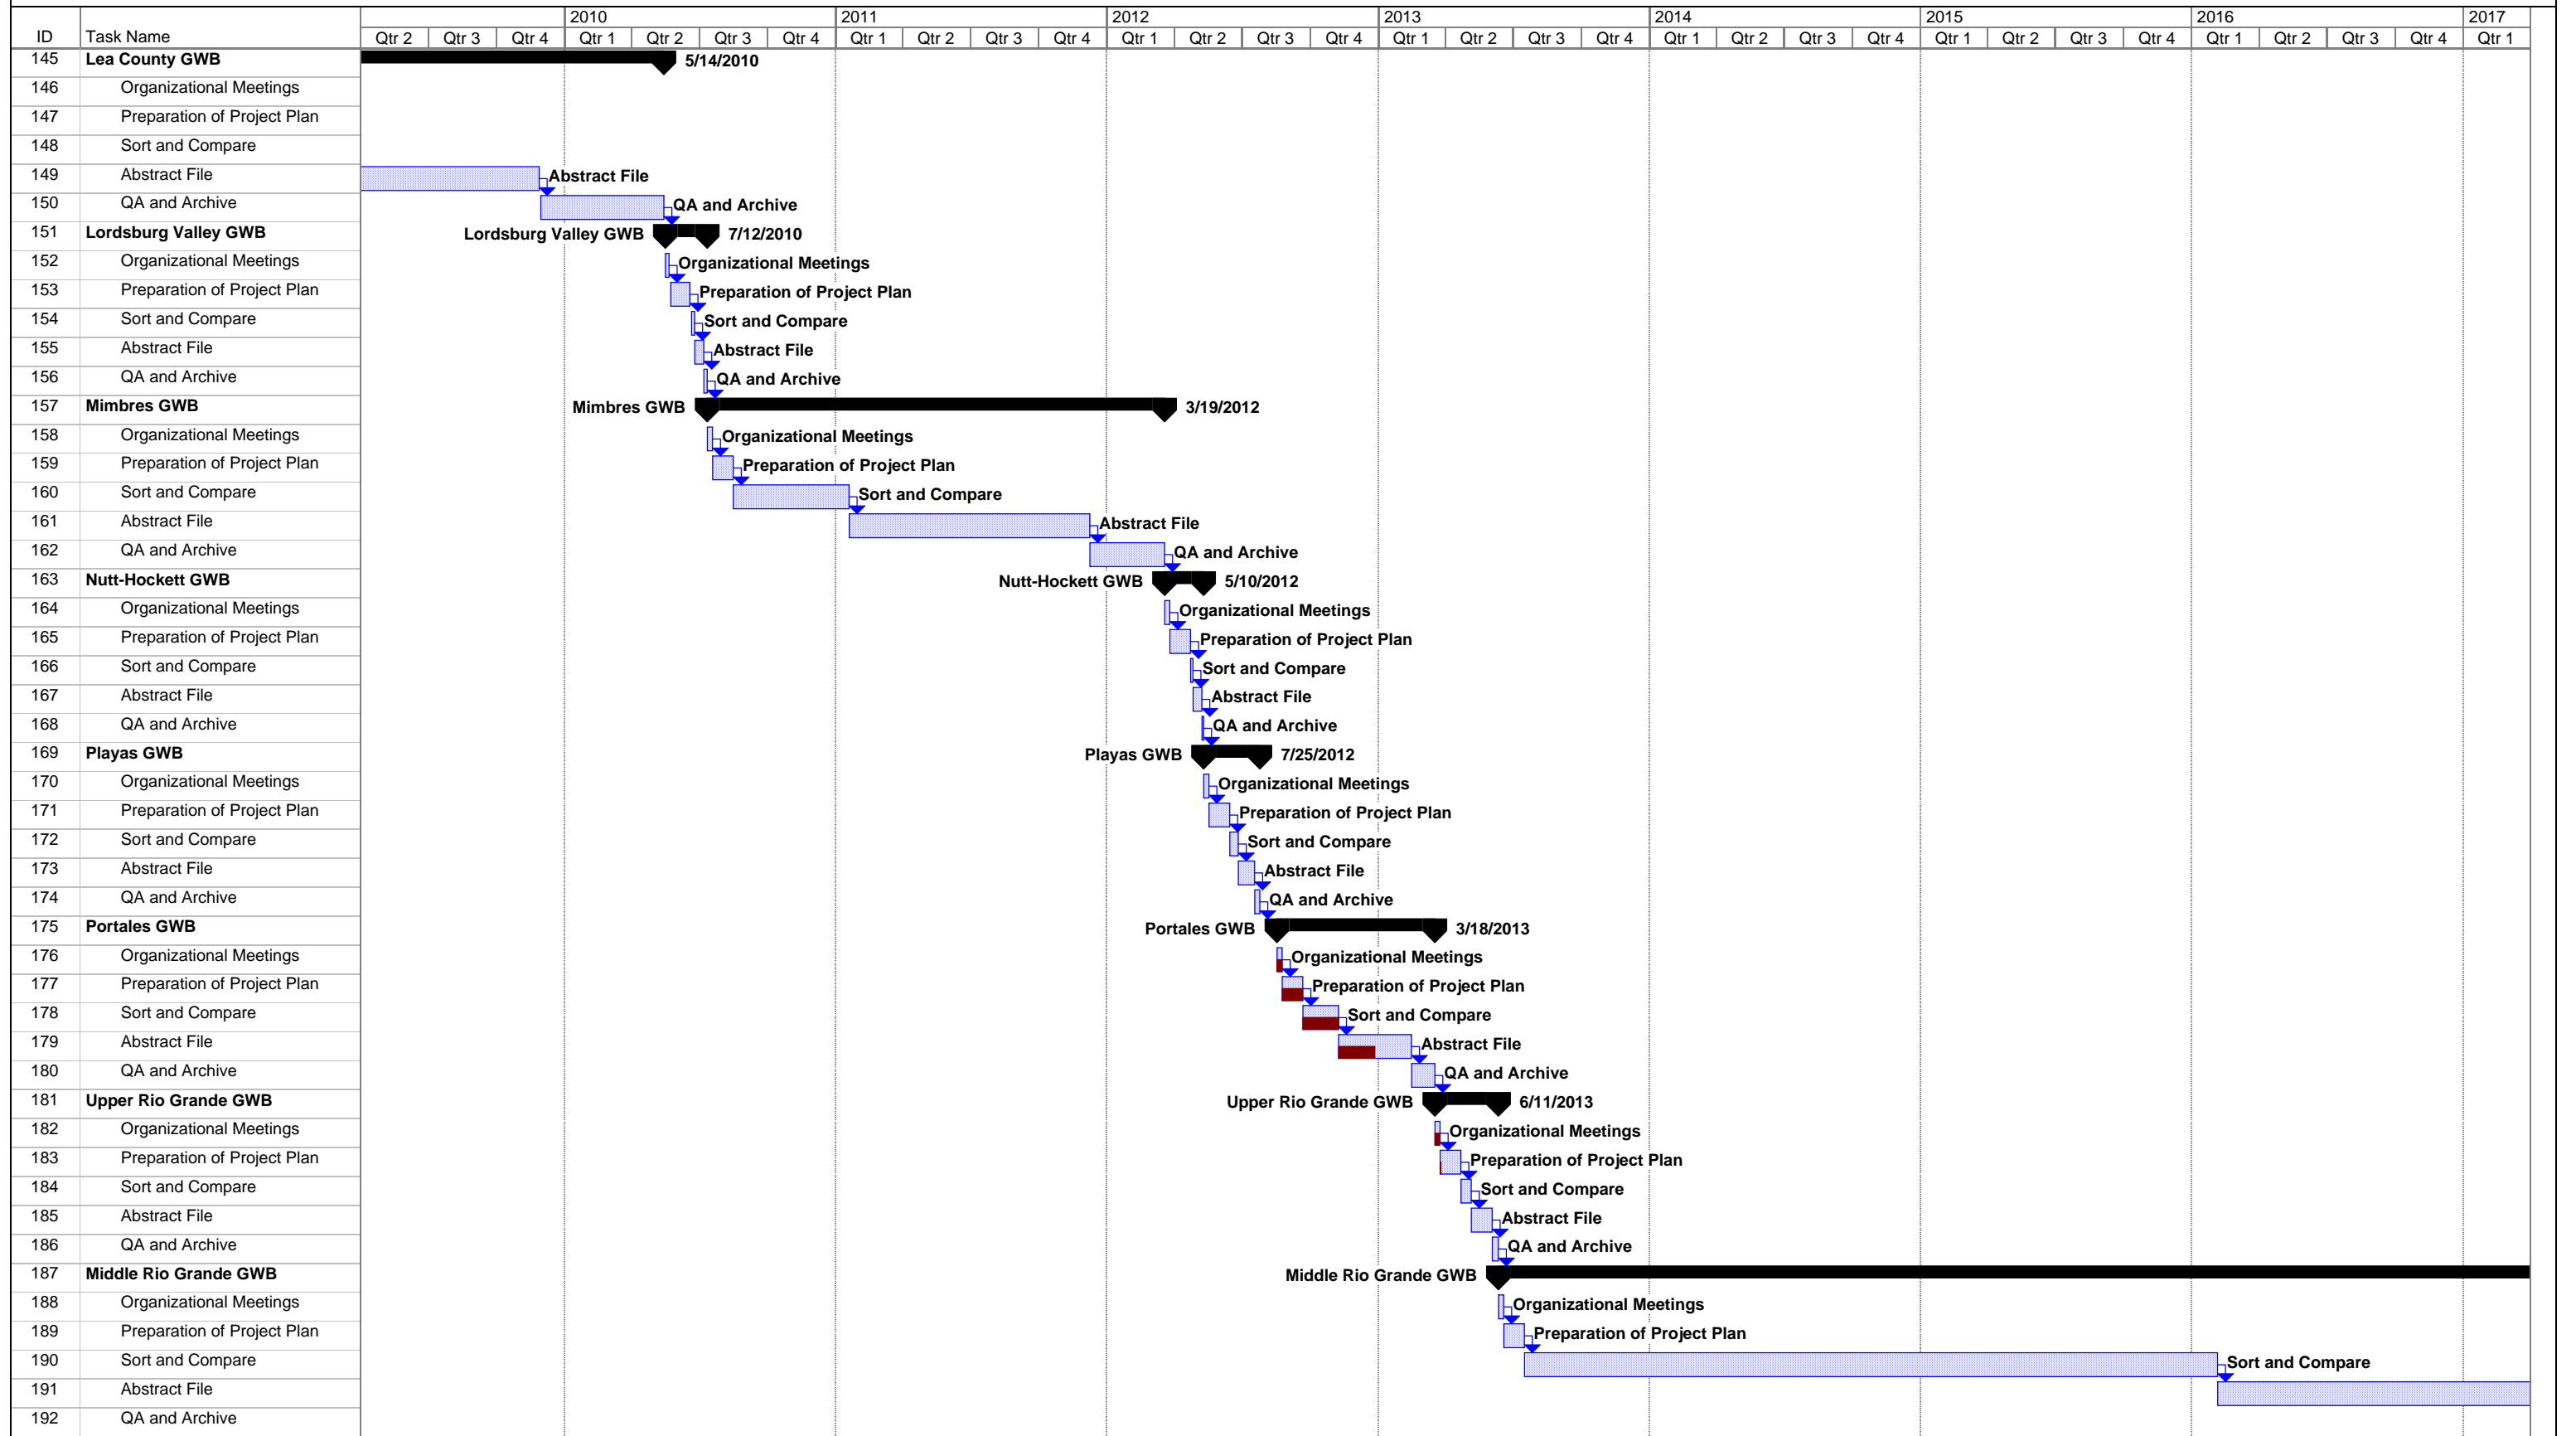

## WATERS (GROUND WATER BASINS)

ID	Task Name	2018			2019				2020				2021				2022				2023				2024				2025	
		Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	
145	<b>Lea County GWB</b>																													
146	Organizational Meetings																													
147	Preparation of Project Plan																													
148	Sort and Compare																													
149	Abstract File																													
150	QA and Archive																													
151	<b>Lordsburg Valley GWB</b>																													
152	Organizational Meetings																													
153	Preparation of Project Plan																													
154	Sort and Compare																													
155	Abstract File																													
156	QA and Archive																													
157	<b>Mimbres GWB</b>																													
158	Organizational Meetings																													
159	Preparation of Project Plan																													
160	Sort and Compare																													
161	Abstract File																													
162	QA and Archive																													
163	<b>Nutt-Hockett GWB</b>																													
164	Organizational Meetings																													
165	Preparation of Project Plan																													
166	Sort and Compare																													
167	Abstract File																													
168	QA and Archive																													
169	<b>Playas GWB</b>																													
170	Organizational Meetings																													
171	Preparation of Project Plan																													
172	Sort and Compare																													
173	Abstract File																													
174	QA and Archive																													
175	<b>Portales GWB</b>																													
176	Organizational Meetings																													
177	Preparation of Project Plan																													
178	Sort and Compare																													
179	Abstract File																													
180	QA and Archive																													
181	<b>Upper Rio Grande GWB</b>																													
182	Organizational Meetings																													
183	Preparation of Project Plan																													
184	Sort and Compare																													
185	Abstract File																													
186	QA and Archive																													
187	<b>Middle Rio Grande GWB</b>	1/9/2023																												
188	Organizational Meetings																													
189	Preparation of Project Plan																													
190	Sort and Compare																													
191	Abstract File	Abstract File																												
192	QA and Archive	QA and Archive																												

Project: WATERS  
Date: Thu 11/13/03

Task		Milestone		Rolled Up Task		Rolled Up Progress		External Tasks		Group By Summary	
Progress		Summary		Rolled Up Milestone		Split		Project Summary			

### WATERS (GROUND WATER BASINS)

ID	Task Name	2018				2019				2020				2021				2022				2023				2024				2025	
		Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1		
193	<b>Roswell Artesian GWB</b>																														
194	Organizational Meetings																														
195	Preparation of Project Plan																														
196	Sort and Compare																														
197	Abstract File																														
198	QA and Archive																														
199	<b>San Simon GWB</b>																														
200	Organizational Meetings																														
201	Preparation of Project Plan																														
202	Sort and Compare																														
203	Abstract File																														
204	QA and Archive																														
205	<b>Tucumcari GWB</b>																														
206	Organizational Meetings																														
207	Preparation of Project Plan																														
208	Sort and Compare																														
209	Abstract File																														
210	QA and Archive																														

