

WATERS (SURFACE WATER BASINS)

ID	Task Name	Duration	Start	Finish	% Complete	Predk	2003				2004				2005				2006				2007				2008							
							Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1							
1	Sandia SWB	27.88 days	Mon 8/25/03	Thu 10/2/03	100%																													
2	Organizational Meetings	5 days	Mon 8/25/03	Fri 8/29/03	100%																													
3	Preparation of Project Plan	20 days	Tue 9/2/03	Mon 9/29/03	100%	2																												
4	Sort and Compare	6 hrs	Tue 9/30/03	Tue 9/30/03	100%	3																												
5	Abstract File	13 hrs	Tue 9/30/03	Thu 10/2/03	100%	4																												
6	QA and Archive	4 hrs	Thu 10/2/03	Thu 10/2/03	100%	5																												
7	Upper Rio Grande SWB	158.63 days	Mon 2/17/03	Tue 9/30/03	30%																													
8	Organizational Meetings	5 days	Mon 2/17/03	Fri 2/21/03	100%																													
9	Preparation of Project Plan	20 days	Mon 2/24/03	Fri 3/21/03	100%	8																												
10	Sort and Compare	132 hrs	Mon 3/24/03	Tue 4/15/03	100%	9																												
11	Abstract File	273 hrs	Tue 4/15/03	Tue 6/3/03	18%	10																												
12	QA and Archive	83 days	Tue 6/3/03	Tue 9/30/03	0%	11																												
13	San Juan SWB	50.13 days	Mon 8/25/03	Wed 11/5/03	0%																													
14	Organizational Meetings	5 days	Mon 8/25/03	Fri 8/29/03	0%																													
15	Preparation of Project Plan	20 days	Tue 9/2/03	Mon 9/29/03	0%	14																												
16	Sort and Compare	54 hrs	Tue 9/30/03	Wed 10/8/03	0%	15																												
17	Abstract File	113 hrs	Wed 10/8/03	Wed 10/29/03	0%	16																												
18	QA and Archive	34 hrs	Wed 10/29/03	Wed 11/5/03	0%	17																												
19	Virден Valley SWB	31.38 days	Tue 9/2/03	Thu 10/16/03	50%																													
20	Organizational Meetings	5 days	Tue 9/2/03	Mon 9/8/03	100%																													
21	Preparation of Project Plan	20 days	Tue 9/9/03	Mon 10/6/03	53%	20																												
22	Sort and Compare	14 hrs	Tue 10/7/03	Wed 10/8/03	0%	21																												
23	Abstract File	28 hrs	Wed 10/8/03	Wed 10/15/03	0%	22																												
24	QA and Archive	9 hrs	Wed 10/15/03	Thu 10/16/03	0%	23																												
25	Upper Pecos SWB	34.25 days	Mon 9/29/03	Tue 11/18/03	20%																													
26	Organizational Meetings	5 days	Mon 9/29/03	Fri 10/3/03	100%																													
27	Preparation of Project Plan	20 days	Mon 10/6/03	Mon 11/3/03	9%	26																												
28	Sort and Compare	20 hrs	Tue 11/4/03	Thu 11/6/03	0%	27																												
29	Abstract File	41 hrs	Thu 11/6/03	Fri 11/14/03	0%	28																												
30	QA and Archive	13 hrs	Fri 11/14/03	Tue 11/18/03	0%	29																												
31	Lower Rio Grande SWB (FIX)	25.38 days	Tue 11/18/03	Fri 12/26/03	0%	30																												
32	Organizational Meetings	5 days	Tue 11/18/03	Tue 11/25/03	0%																													
33	Preparation of Project Plan	20 days	Tue 11/25/03	Fri 12/26/03	0%	32																												
34	Sort and Compare	1 hr	Fri 12/26/03	Fri 12/26/03	0%	33																												
35	Abstract File	1 hr	Fri 12/26/03	Fri 12/26/03	0%	34																												
36	QA and Archive	1 hr	Fri 12/26/03	Fri 12/26/03	0%	35																												
37	Bluewater SWB	27 days	Fri 12/26/03	Tue 2/3/04	0%	36																												
38	Organizational Meetings	5 days	Fri 12/26/03	Fri 1/2/04	0%																													
39	Preparation of Project Plan	20 days	Fri 1/2/04	Fri 1/30/04	0%	38																												
40	Sort and Compare	4 hrs	Fri 1/30/04	Mon 2/2/04	0%	39																												
41	Abstract File	9 hrs	Mon 2/2/04	Tue 2/3/04	0%	40																												
42	QA and Archive	3 hrs	Tue 2/3/04	Tue 2/3/04	0%	41																												

Project: WATERS
Date: Fri 11/14/03

Task		Milestone		Rolled Up Task		Rolled Up Progress		External Tasks		Group By Summary	
Progress		Summary		Rolled Up Milestone		Split		Project Summary			

P:\040078\FPE\Schedule\WATERS Surface.mpp Page 1


WATERS (SURFACE WATER BASINS)

ID	Task Name	Duration	Start	Finish	% Complete	Predt	2003				2004				2005				2006				2007				2008							
							Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1							
43	Estancia SWB	29.25 days	Tue 2/3/04	Mon 3/15/04	0%	42																												
44	Organizational Meetings	5 days	Tue 2/3/04	Tue 2/10/04	0%																													
45	Preparation of Project Plan	20 days	Tue 2/10/04	Tue 3/9/04	0%	44																												
46	Sort and Compare	9 hrs	Tue 3/9/04	Wed 3/10/04	0%	45																												
47	Abstract File	19 hrs	Wed 3/10/04	Mon 3/15/04	0%	46																												
48	QA and Archive	6 hrs	Mon 3/15/04	Mon 3/15/04	0%	47																												
49	Canadian River & Dry Cimmaron SW	51.5 days	Mon 3/15/04	Wed 5/26/04	0%	48																												
50	Organizational Meetings	5 days	Mon 3/15/04	Mon 3/22/04	0%																													
51	Preparation of Project Plan	20 days	Mon 3/22/04	Mon 4/19/04	0%	50																												
52	Sort and Compare	57 hrs	Mon 4/19/04	Wed 4/28/04	0%	51																												
53	Abstract File	119 hrs	Thu 4/29/04	Wed 5/19/04	0%	52																												
54	QA and Archive	36 hrs	Wed 5/19/04	Wed 5/26/04	0%	53																												
55	Gila - San Francisco SWB	33.38 days	Wed 5/26/04	Mon 7/12/04	0%	54																												
56	Organizational Meetings	5 days	Wed 5/26/04	Wed 6/2/04	0%																													
57	Preparation of Project Plan	20 days	Wed 6/2/04	Wed 6/30/04	0%	56																												
58	Sort and Compare	18 hrs	Wed 6/30/04	Fri 7/2/04	0%	57																												
59	Abstract File	38 hrs	Fri 7/2/04	Fri 7/9/04	0%	58																												
60	QA and Archive	11 hrs	Fri 7/9/04	Mon 7/12/04	0%	59																												
61	Hot Springs SWB	25.88 days	Mon 7/12/04	Tue 8/17/04	0%	60																												
62	Organizational Meetings	5 days	Mon 7/12/04	Mon 7/19/04	0%																													
63	Preparation of Project Plan	20 days	Mon 7/19/04	Mon 8/16/04	0%	62																												
64	Sort and Compare	2 hrs	Mon 8/16/04	Mon 8/16/04	0%	63																												
65	Abstract File	4 hrs	Tue 8/17/04	Tue 8/17/04	0%	64																												
66	QA and Archive	1 hr	Tue 8/17/04	Tue 8/17/04	0%	65																												
67	Hueco SWB	27.25 days	Tue 8/17/04	Thu 9/23/04	0%	66																												
68	Organizational Meetings	5 days	Tue 8/17/04	Tue 8/24/04	0%																													
69	Preparation of Project Plan	20 days	Tue 8/24/04	Tue 9/21/04	0%	68																												
70	Sort and Compare	5 hrs	Tue 9/21/04	Wed 9/22/04	0%	69																												
71	Abstract File	10 hrs	Wed 9/22/04	Thu 9/23/04	0%	70																												
72	QA and Archive	3 hrs	Thu 9/23/04	Thu 9/23/04	0%	71																												
73	Gallup SWB	33.38 days	Thu 9/23/04	Wed 11/10/04	0%	72																												
74	Organizational Meetings	5 days	Thu 9/23/04	Thu 9/30/04	0%																													
75	Preparation of Project Plan	20 days	Thu 9/30/04	Thu 10/28/04	0%	74																												
76	Sort and Compare	18 hrs	Thu 10/28/04	Tue 11/2/04	0%	75																												
77	Abstract File	38 hrs	Tue 11/2/04	Mon 11/8/04	0%	76																												
78	QA and Archive	11 hrs	Mon 11/8/04	Wed 11/10/04	0%	77																												
79	Roswell Artesian SWB	61.63 days	Wed 11/10/04	Thu 2/3/05	0%	78																												
80	Organizational Meetings	5 days	Wed 11/10/04	Wed 11/17/04	0%																													
81	Preparation of Project Plan	20 days	Wed 11/17/04	Wed 12/15/04	0%	80																												
82	Sort and Compare	79 hrs	Wed 12/15/04	Wed 12/29/04	0%	81																												
83	Abstract File	164 hrs	Wed 12/29/04	Wed 1/26/05	0%	82																												
84	QA and Archive	50 hrs	Wed 1/26/05	Thu 2/3/05	0%	83																												

Project: WATERS Date: Fri 11/14/03	Task	Milestone	Rolled Up Task	Rolled Up Progress	External Tasks	Group By Summary
	Progress	Summary	Rolled Up Milestone	Split	Project Summary	

WATERS (SURFACE WATER BASINS)

ID	Task Name	Duration	Start	Finish	% Complete	Predt	2003				2004				2005				2006				2007				2008						
							Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1						
85	Carlsbad SWB	46 days	Thu 2/3/05	Fri 4/8/05	0%	84									Carlsbad SWB	4/8/2005																	
86	Organizational Meetings	5 days	Thu 2/3/05	Thu 2/10/05	0%																												
87	Preparation of Project Plan	20 days	Thu 2/10/05	Thu 3/10/05	0%	86																											
88	Sort and Compare	45 hrs	Thu 3/10/05	Fri 3/18/05	0%	87																											
89	Abstract File	94 hrs	Fri 3/18/05	Tue 4/5/05	0%	88																											
90	QA and Archive	29 hrs	Tue 4/5/05	Fri 4/8/05	0%	89																											
91	Hondo SWB	27.13 days	Fri 4/8/05	Tue 5/17/05	0%	90									Hondo SWB	5/17/2005																	
92	Organizational Meetings	5 days	Fri 4/8/05	Fri 4/15/05	0%																												
93	Preparation of Project Plan	20 days	Fri 4/15/05	Fri 5/13/05	0%	92																											
94	Sort and Compare	5 hrs	Fri 5/13/05	Mon 5/16/05	0%	93																											
95	Abstract File	9 hrs	Mon 5/16/05	Tue 5/17/05	0%	94																											
96	QA and Archive	3 hrs	Tue 5/17/05	Tue 5/17/05	0%	95																											
97	Penasco SWB	26.38 days	Wed 5/18/05	Thu 6/23/05	0%	96									Penasco SWB	6/23/2005																	
98	Organizational Meetings	5 days	Wed 5/18/05	Tue 5/24/05	0%																												
99	Preparation of Project Plan	20 days	Wed 5/25/05	Tue 6/21/05	0%	98																											
100	Sort and Compare	3 hrs	Wed 6/22/05	Wed 6/22/05	0%	99																											
101	Abstract File	6 hrs	Wed 6/22/05	Thu 6/23/05	0%	100																											
102	QA and Archive	2 hrs	Thu 6/23/05	Thu 6/23/05	0%	101																											
103	Fort Sumner SWB	50.13 days	Thu 6/23/05	Thu 9/1/05	0%	102									Fort Sumner SWB	9/1/2005																	
104	Organizational Meetings	5 days	Thu 6/23/05	Thu 6/30/05	0%																												
105	Preparation of Project Plan	20 days	Thu 6/30/05	Thu 7/28/05	0%	104																											
106	Sort and Compare	54 hrs	Thu 7/28/05	Mon 8/8/05	0%	105																											
107	Abstract File	113 hrs	Mon 8/8/05	Fri 8/26/05	0%	106																											
108	QA and Archive	34 hrs	Fri 8/26/05	Thu 9/1/05	0%	107																											
109	Hagerman Canal SWB	25.88 days	Thu 9/1/05	Fri 10/7/05	0%	108									Hagerman Canal SWB	10/7/2005																	
110	Organizational Meetings	5 days	Thu 9/1/05	Thu 9/8/05	0%																												
111	Preparation of Project Plan	20 days	Thu 9/8/05	Thu 10/6/05	0%	110																											
112	Sort and Compare	2 hrs	Thu 10/6/05	Thu 10/6/05	0%	111																											
113	Abstract File	4 hrs	Thu 10/6/05	Fri 10/7/05	0%	112																											
114	QA and Archive	1 hr	Fri 10/7/05	Fri 10/7/05	0%	113																											
115	Jal SWB	25.38 days	Fri 10/7/05	Fri 11/11/05	0%	114									Jal SWB	11/11/2005																	
116	Organizational Meetings	5 days	Fri 10/7/05	Fri 10/14/05	0%																												
117	Preparation of Project Plan	20 days	Fri 10/14/05	Fri 11/11/05	0%	116																											
118	Sort and Compare	1 hr	Fri 11/11/05	Fri 11/11/05	0%	117																											
119	Abstract File	1 hr	Fri 11/11/05	Fri 11/11/05	0%	118																											
120	QA and Archive	1 hr	Fri 11/11/05	Fri 11/11/05	0%	119																											
121	Middle Rio Grande SWB	165.63 days	Fri 11/11/05	Mon 7/3/06	0%	120									Middle Rio Grande SWB	7/3/2006																	
122	Organizational Meetings	5 days	Fri 11/11/05	Fri 11/18/05	0%																												
123	Preparation of Project Plan	20 days	Fri 11/18/05	Fri 12/16/05	0%	122																											
124	Sort and Compare	304 hrs	Fri 12/16/05	Wed 2/8/06	0%	123																											
125	Abstract File	630 hrs	Wed 2/8/06	Tue 5/30/06	0%	124																											
126	QA and Archive	191 hrs	Tue 5/30/06	Mon 7/3/06	0%	125																											

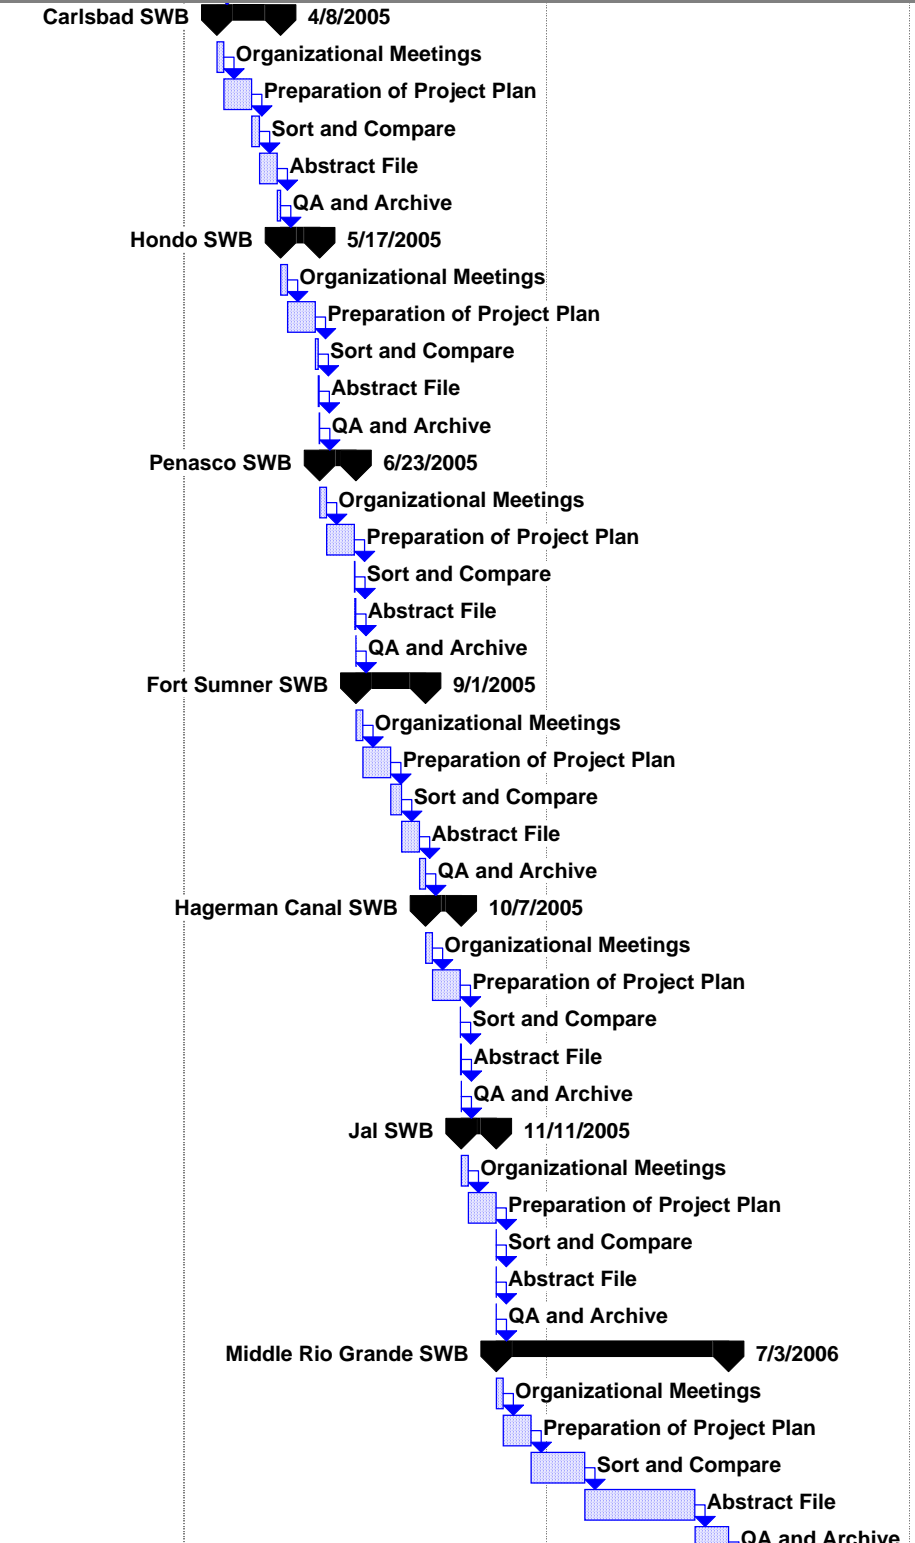

Project: WATERS Date: Fri 11/14/03	Task	Milestone	Rolled Up Task	Rolled Up Progress	External Tasks	Group By Summary
	Progress	Summary	Rolled Up Milestone	Split	Project Summary	

